

Monthly Progress Report – JUNE-2024
La CITADEL PROJECT, VISAKHAPATNAM

Presented By:



Presented To:




SL. NO	DESCRIPTION	PAGE
1	PROJECT BRIEF	4-7
2	MANAGEMENT SYNOPSIS	
2.1	Overall Project Time lines	8
2.2	Design Management	9
2.3	Major Mile stone Schedule	10
2.4	Quality Management	11
2.5	Manpower Histogram update	12
3	OHSA REPORT	13-14
4	WORK STATUS REPORT	15
5	PROJECT PROGRESS PHOTOGRAPHS	16-117
6	THANK YOU	118

LA CITADEL
by



SITE KEY PLAN

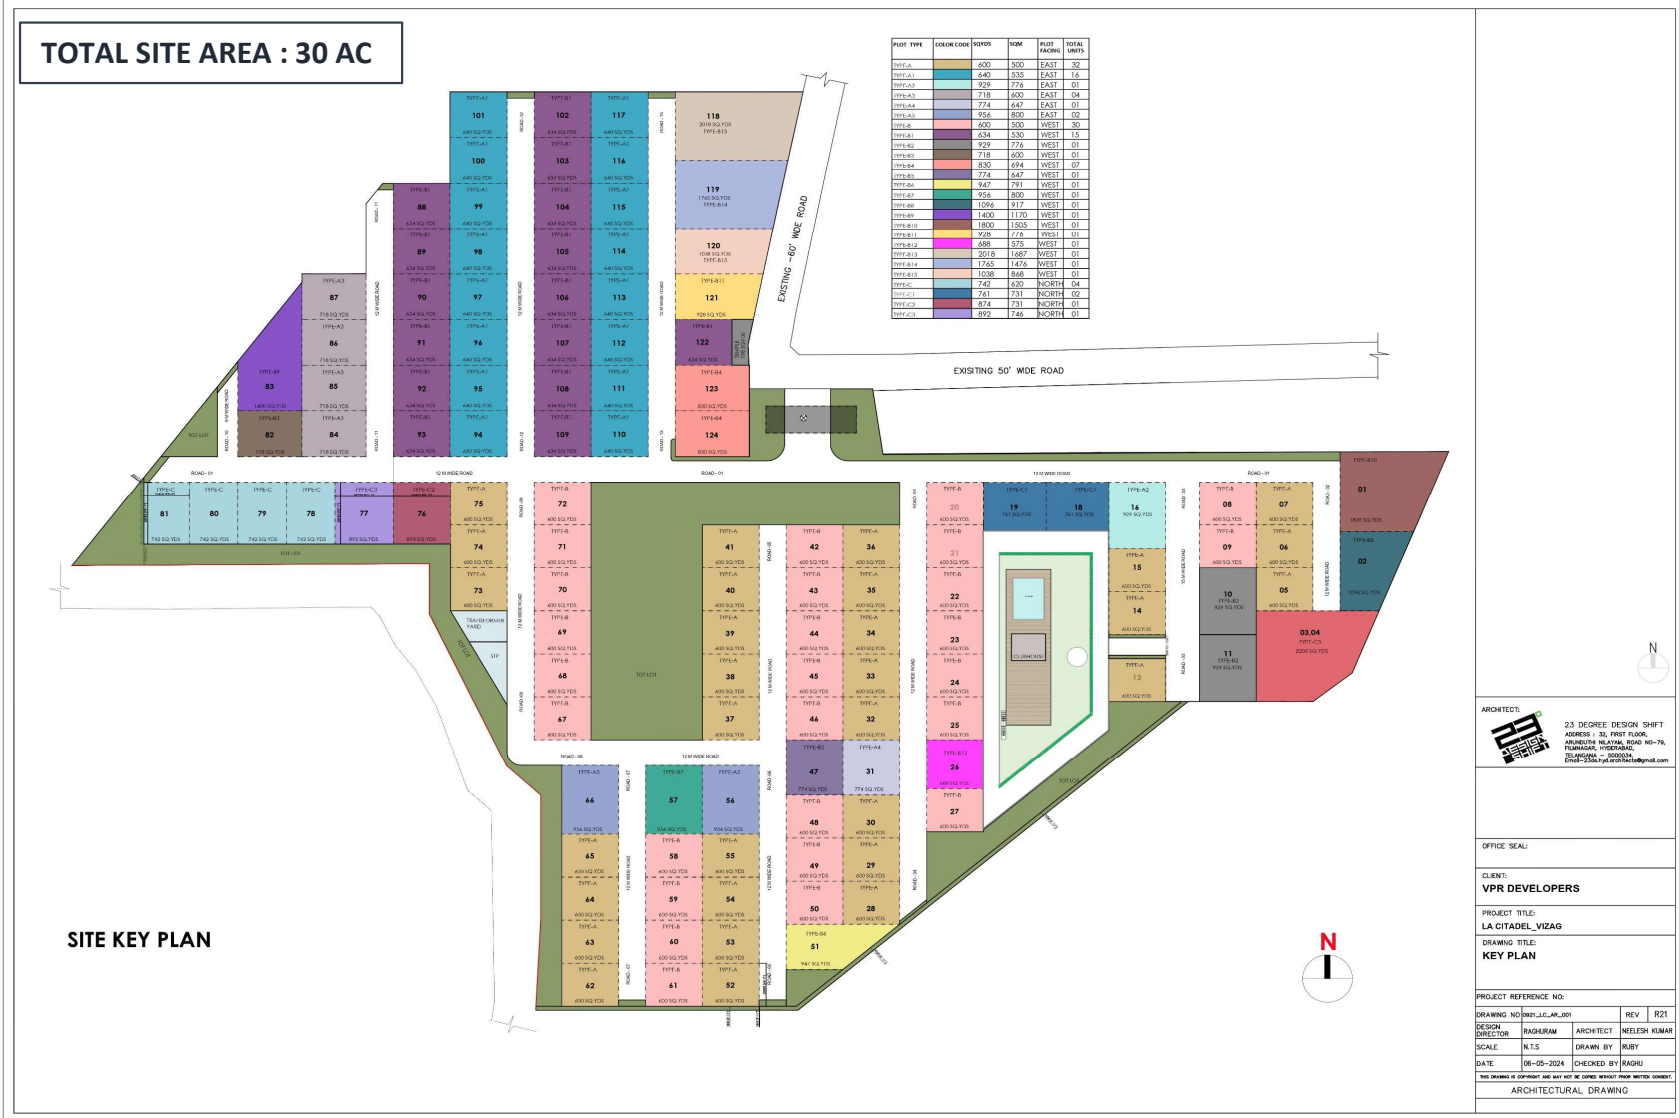

SITE KEY PLAN



LA CITADEL
by

NAME OF THE PROJECT	La CITADEL
Location	Rushikonda, Visakhapatnam
Total Villas	121 No's
Total Built up Area - Villas	10.56 Lakhs Sq.Ft
Club House built up area	70000 Sqft
Total Land Area	30 Acre (Over all area)

ARCHITECTS,CONSULTANTS & CONTRACTORS

Client	M/s. VPR & Concrete Infra Project
Principal Architect	M/s. 23° DESIGN SHIFT
Structural Consultant	M/s. ID Structural Consultants
Landscape Consultant	M/s. Naveen Associates
MEP Consultant	M/s. Ennovative Design Consultants
Civil – Contractor	<ol style="list-style-type: none"> 1. Burri Guravaiah 2. Venkata Reddy 3. Y Brahmaiah 4. Sita Ram 5. JK INFRA 6. Sruthika Construction 7. Pavan Suta Developers 8. Shree Sai Ambica 9. SB Projects 10. Associated Infra projects 11. Sree Sree Enterprises
Electrical & Plumbing Contractor	M/s. Mallesh & Manoj

LA CITADEL
by



1.1 VILLA PROJECT

Total Built up Area	10.56 Lakh Sq.Ft
No. of floors	G + 2 Floors : Foundation designed for G + 2 floors
Total Villas	121 Nos.
Villas Plot area	600,634,640,661,668,694,718,742,761,774,830,874,884,928,947,956,1053,1400,1800 Sq.yds
Additional Features	Home Theatre, Powder room, Puja Room, deck, Store, Lift Lobby, Servant Room, 3 Car Parking etc.,
Ground Floor	Living, Drawing, Dining, Guest Bed , Store, Kitchen etc.,
First Floor	Lounge, Puja, Master Bed, Children Bed, Deck etc.,
Second Floor	Master Bed, Lounge, Home Theatre and open to sky area.
Floor to Floor heights	Ground Floor-14 Feet, First Floor-13Feet and Second Floor-13 Feet

1.2 CLUB HOUSE

Total Built up Area	70000Sq.Ft
No. of floors	Stilt + 3 Floors : Foundation designed for G + 3 floors
Additional Features	Theatre, Meeting room, Guest Bedrooms, Changing Rooms etc.,
Stilt Floor	100 Parking & Badminton Court.
First Floor	Coffee Shop, Waiting Area, Office Space, Prefunction Area, Banquet Hall etc.,
Second Floor	Multi Purpose Hall, Indoor Games, Lounge etc.,
Third Floor	Gym, Saloon/Spa, Cafe & Bar etc.,
Terrace Floor	Swimming Pool & Party Deck

2.0 MANAGEMENT SYNOPSIS

2.1 Over All Project Time lines

Sl. No	Description	Target Date	Anticipated / Actual	Cumulative % Completion up to Previous Month	Cumulative % Completion up to Reporting Month	Remarks
1	Project Start	10-JULY-23	02-NOV-23			L
2	Retaining walls	30-DEC-24		46	51	
3	Shell & Core	13-04-25		31.2	38.9	
4	Final handover Overall	09-SEP-25		12	14	

2.0 MANAGEMENT SYNOPSIS

2.2 Design Management

I) Vendor Finalization

1	Civil vendor finalized	25-May-23	01-July-23 - T&J INFRA 01-June-23 - B GURAVIAH 01-June-23 - SVR Const.. 01-June-23 - Srinivasa const.. 01-may-23 - Pavan Sutta Cen. 01-Apr-24 - Sree Sai Ambica 01-May-24 – Darthi Infra	7 Vendors finalized for villas Shell & Core works. 2 Vendor finalized for reattaining walls 2 Vendor finalized for Excavation & Blasting.
2	Plumbing Vendor Finalization	10-NOV-23	10-08-23	Manoj
3	Electrical vendor Finalization	10-NOV-23	10-08-23	Mallesh
4	Landscape vendor Finalization	15-JULY-23		Naveen Association
5	Interior vendor Finalization			Yet to be Finalize

II) Procurement

1	Steel – RINL/VIZAG		Received as on 30 JUN 2024 as 1876.4 MT received
2	Cement		Received as on 30 JUN 2024- 13210-PPC 560-OPC Bags received.
3	Concrete		Received as on 30 JUN 2024 – RCC – 18656.5 M ³ & PCC – 2713 M ³

2.0 MANAGEMENT SYNOPSIS

2.3 Major Milestone Schedule

Sl. No.	Description	Villa Project		Club House		Entrance Arch	
		Start/actual	End/actual	Start/actual	End/actual	Start/actual	End/actual
1	Foundation	02-JUNE-23	02-JUNE-24	01-MAR-23		01-FEB-24	
		02-NOVE-23	02-				
		Work in Progress		Yet to Start		Yet to Start	
2	Super structure	26-AUG-23					
		26-SEP-23					
		Work in Progress		Yet to Start		Yet to Start	
3	Finishing	27-10-23					
		Yet to Start		Yet to Start		Yet to Start	
4	Interior Works						
		Yet to Start		Yet to Start		Yet to Start	
5	Services Works						
		Yet to Start		Yet to Start		Yet to Start	
6	Final handover						
		02-11-2023	04-09-2025				

LA CITADEL
by


2.0 MANAGEMENT SYNOPSIS

2.4 Quality Management

Package	Items	Result	Remarks
Civil, Structural works	Cement / Steel /Water/Fine aggregate/Coarse aggregate	Ok	
	Design Mix	Ok	
	Construction quality	Ok	
	Concreting	Ok	
	Shuttering	Ok	
	Block work/Brick Work	OK	
	Plinth Filling / PCC	OK	
Over all Quality		GOOD	

2.0 MANAGEMENT SYNOPSIS

2.5 Manpower Histogram update

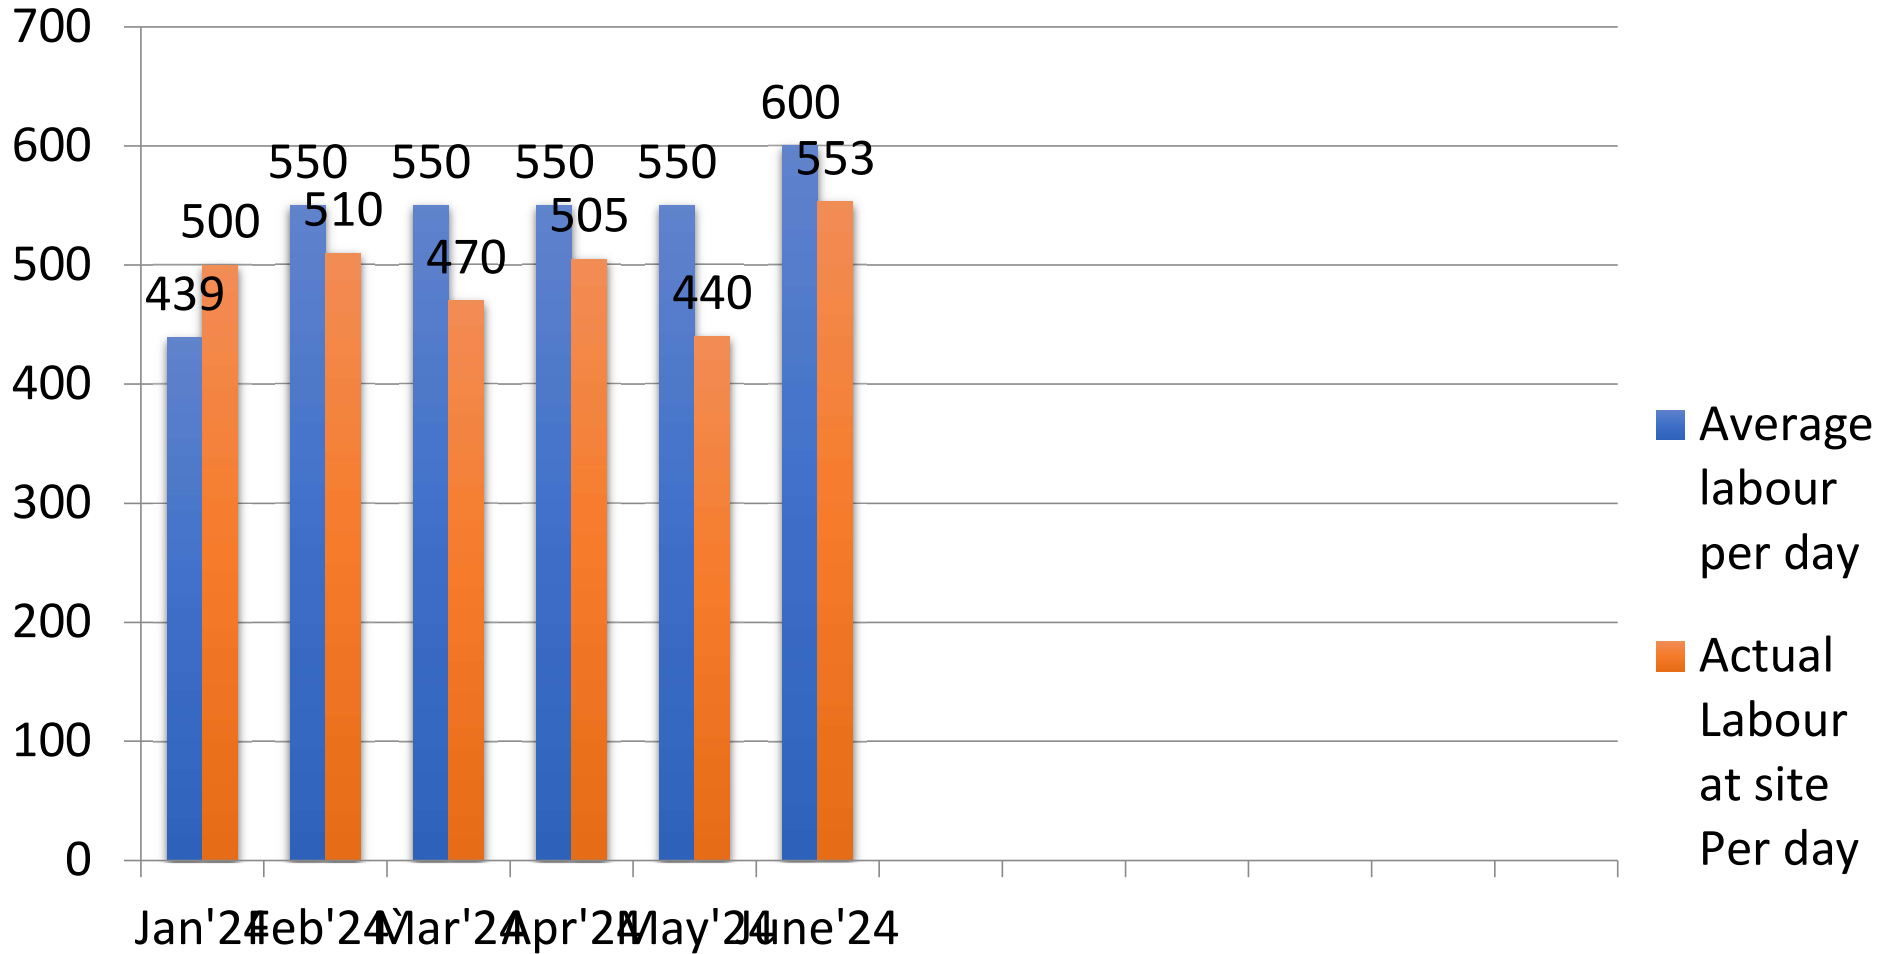

3.0 OHSA REPORT

Sl.No	Description	Status
1	Cumulative Man-hours worked till date	898400 Hrs.
2	No. of Reportable Accidents on project	0
3	No. of Near Misses	0
4	No. of Lost Work Day (LWD) cases	0
5	No. of Safety Inspections conducted	4
6	No. of Safety Audits conducted	4
	Electrical inspection	2
	Plant Machineries	1
7	No. of Safety Infraction Notices	2
8	No. of Fire extinguishers available at site Co2-5,ABC-5	10
9	No. of Training sessions conducted	4
	a) Video show training	1
	b) Medical Camp	1
	c) Emergency Mock drill Training	2
	d) Fire Fighting training (For Lab ours)	1
	e) First Aid training	1

3.0 OHSE REPORT

Sl.No	Description	Status
10	No. of Safety Pep talks/ Tool Box meeting, Safety Inductions conducted this month	4
11	Total number of Safety Permits Issued this month	210
12	No. of Safety sign boards displayed at site	20
13	Housekeeping practices (Excellent/ V Good/ Good/ Average/ Poor)	Good
14	Labour Facility (Sanitation & Resting area)	Good
15	Equipment, Machinery & Tools inspection (Satisfactory/ Not)	Satisfactory
16	Physical condition of the PPE in usage (Good/ Average/ Poor)	Good
17	License and vehicle documents available (if applicable)	Available
18	Percentage compliance on the usage of PPE by workers	100%
19	Overall EHS implementation (Excellent/ V Good/ Good/ Average/ Poor)	Good

4.0 WORK STATUS REPORT

Sl.No.	Description of works	Total Villas	UNITS	Till Date Completed	% of Completed	Remarks
1	Excavation	121	No.s	96	79.34%	
2	ATT	121	No.s	95	78.51%	
3	Footing PCC	121	No.s	95	78.51%	
4	Footing RCC	121	No.s	93	76.86%	
5	Neck Columns	121	No.s	87	71.90%	
6	Soil Back Filling	121	No.s	72	59.50%	
7	Plinth Beam Filling	121	No.s	63	52.07%	
8	Grade Slab	121	No.s	61	50.41%	
9	G.F Columns	121	No.s	54	44.63%	
10	1ST Slab	121	No.s	47	38.84%	
11	G.F BRICKWORK	121	No.s	10	8.26%	
12	F.F Columns	121	No.s	36	29.75%	
13	2nd Slab	121	No.s	27	22.31%	
14	F.F BRICKWORK	121	No.s	6	4.96%	
15	S.F Columns	121	No.s	17	14.05%	
16	3rd SLAB	121	No.s	12	9.92%	
17	S.F BRICKWORK	121	No.s	2	1.65%	

5. PROJECT PHOTOGRAPHS



SITE KEY PLAN

VENKAT REDDY- CONTRACTOR 13 Villas (Villa no: 5 TO 09,20-27)– Contract Shell & Core Works

La CITADEL/MPR



Villa No-5 1st Concrete completed



Villa No-6 F.F brick work Completed



Villa No-7 2nd Slab Concrete Completed & G.F Brick Work WIP



Villa No-8 1st Slab Concrete Completed & G.F Brickwork WIP



Villa No-9 3rd Slab Concrete Completed & G.F WIP



Villa No-14 Footings WIP



Villa No-15 Footing Concrete Completed



Villa No-18 Footing Shuttering WIP



Villa No-19 Footing PCC Concrete Completed



Villa No-20 Grade Slab Concrete Completed



Villa No-21 Plinth Beam Backfilling Completed



Villa No-22 1st Slab Shuttering WIP



LA CITADEL
by



Villa No-23 1st Slab Shuttering WIP



Villa No-24 F.F Columns Concrete Completed



Villa No-25 2nd Slab Concrete Completed & G.F Brickwork WIP



La CITADEL/MPR

LA CITADEL
by

VPR BUILDERS | **CONCRETE ANFRA**

Villa No-26 2nd Slab Concrete Completed & G.F Brickwork WIP



Villa No-27 2nd Slab Concrete & F.F Brickwork WIP





SHREE SAI AMBICA- CONTRACTOR

16 Villas (Villa no: 28-36 & 118-124)– Contract Shell & Core Works

La CITADEL/MPR

LA CITADEL
by



Villa No-29 F.F Columns Concrete Completed



Villa No-30 2nd Slab Concrete Completed



Villa No-31 Grade Slab Concrete Completed



Villa No-32 Rolling WIP



Villa No-33 Rolling WIP



Villa No-34 Compound Wall Concrete WIP



Villa No-122 Soil Backfilling WIP



Villa No-124 Neck Columns Concrete Completed





SITE KEY PLAN

GURUVAIAH- CONTRACTOR 30 Villas (Villa no: 37 to 66)– Contract Shell & Core Works

La CITADEL/MPR

LA CITADEL
by



Villa No-37 S.F Brick Work WIP



Villa No-38 External Plastering Completed S.F Internal Plastering WIP



Villa No-39 External Texture & internal Putty WIP



Villa No-40 Third Slab Completed & F.F Brick Work WIP



Villa No-41 3rd Slab Concrete & S.F Brick Work Completed



Villa No-42 External Plastering WIP



Villa No-43 S.F Brickwork WIP



Villa No-44 3rd Slab Concrete Completed & F.F Brickwork WIP



Villa No-45 3rd Slab Shuttering WIP & G.F Brickwork WIP



Villa No-46 F.F Columns Concrete Completed & G.F Brickwork WIP



LA CITADEL
by



Villa No-47 1st Slab Concrete Completed & G.F WIP



Villa No-48 1st Slab Concrete Completed & G.F Brickwork WIP



LA CITADEL
by



Villa No-49 1st Slab Completed & G.F Brickwork WIP



Villa No-50 1st Slab Concrete Completed & G.F Brickwork WIP



Villa No-53 2nd Slab WIP



Villa No-54 F.F Columns WIP



Villa No-55 G.F Columns Concrete Completed



Villa No-58 Rolling Completed



Villa No-59 Plinth Beam Brick Work Completed



Villa No: 60 1st Slab Concrete Completed





SITE KEY PLAN

BRAHMAIAH- CONTRACTOR 27 Villas (Villa no: 67 to 93)– Contract Shell & Core Works

La CITADEL/MPR



LA CITADEL
by

Villa No- 67 Soil Backfilling Completed



Villa No- 68 S.F Columns WIP Completed



Villa No- 69 F.F Columns Concrete Completed



Villa No-70 2nd Slab Shuttering WIP & G.F Brickwork WIP



Villa No- 71 3rd Slab Shuttering WIP & G.F Brickwork Completed



LA CITADEL
by



Villa No- 72 S.F Columns Concrete Completed



Villa No- 73 Soil Backfilling WIP



Villa No- 74 External Plastering WIP



Villa No- 76 Soil Backfilling WIP



Villa No- 79 Footing Excavation WIP



Villa No- 80 Soil backfilling WIP



Villa No- 81 Tie beam WIP



Villa No- 82 Neck Columns Concrete Completed



Villa No- 87 Grade Slab WIP



Villa No- 88 Grade Slab WIP



Villa No- 89 G.F Columns Concrete Completed



Villa No- 90 1st Slab Concrete Completed



Villa No- 91 G.F Columns Concrete Completed



Villa No- 92 1ST Slab Shuttering WIP



Villa No- 93 2ND Slab Shuttering WIP





SITE KEY PLAN

T&J- CONTRACTOR
13 Villas (Villa no: 94 - 98 & 100-117)– Contract Shell & Core Works

La CITADEL/MPR

LA CITADEL
by



Villa No-94 2ND Slab Concrete Completed & F.F Brick Work WIP



Villa No-95 2nd Slab & G.F Brickwork Completed



Villa No-96 G.F Brick Work WIP & S.F columns Concrete Completed



Villa No-97 3rd Slab Shuttering & F.F Brickwork WIP



Villa No-98 3rd Slab Concrete Completed & G.F Brickwork WIP



Villa No-110 2nd Slab Shuttering WIP



Villa No-111 G.F Columns Concrete Completed



Villa No-112 G.F Columns WIP



LA CITADEL
by



Villa No-113 S.F Slab Shuttering WIP



Villa No-114 1st Slab WIP



Villa No-115 Grade Slab Concrete Completed



Villa No-116 Grade Slab Concrete Completed



Villa No-117 Grade Slab Concrete Completed



LA CITADEL
by





SITE KEY PLAN



PAVAN SUTA CENTERING - CONTRACTOR

07 Villas (Villa no: 99-109)– Contract Shell & Core Works

La CITADEL/MPR

LA CITADEL
by



Villa No-99 G.F Columns Concrete Completed & G.F Brickwork WIP



La CITADEL/MPR



Villa No-100 S.F Columns Concrete Completed & G.F Brickwork WIP



La CITADEL/MPR



Villa No-101 F.F Columns Concrete Completed



Villa No-102 Footing Pedestal Concrete Completed



Villa No-103 Soil Backfilling WIP



Villa No-104 Backfilling WIP



Villa No-105 Soil Backfilling WIP



Villa No-106 Backfilling WIP



Villa No-107 Backfilling WIP



Villa No-108 Grade Slab WIP



Villa No-109 Grade Slab Concrete Completed



Villa No- SOUTH WEST NALL SIDE R/W CONCRETE WIP



R/W- SOUTH WEST OFFICE NALL SIDE R/W WIP



LA CITADEL
by



Villa No-76 Retaining Wall Raft WIP



Club House Retaining Wall Raft WIP



Road No-1 Retaining Wall Raft & Wall WIP





THANK YOU
