

Weekly Progress Report No.56 – Oct'24/ 14 – 20

La CITADEL PROJECT, VISAKHAPATNAM

Presented By:



Presented To:



SITE KEY PLAN

TOTAL SITE AREA : 30 AC

| PILOT TYPE | COLOR CODE | NOVPS | SDM | PILOT PAIRING | TOTAL UNITS |
|------------|------------|-------|-------|---------------|-------------|
| TYPE A | 630 | 500 | EAST | 32 | |
| TYPE A | 640 | 500 | EAST | 16 | |
| TYPE A | 640 | 499 | EAST | 01 | |
| TYPE A | 670 | 600 | EAST | 04 | |
| TYPE A | 677 | 647 | EAST | 01 | |
| TYPE A | 736 | 800 | EAST | 02 | |
| TYPE A | 600 | 800 | WEST | 20 | |
| TYPE B | 831 | 500 | WEST | 16 | |
| TYPE B | 929 | 775 | WEST | 01 | |
| TYPE B | 878 | 640 | WEST | 01 | |
| TYPE B | 843 | 697 | WEST | 07 | |
| TYPE B | 776 | 647 | WEST | 01 | |
| TYPE B | 866 | 691 | WEST | 03 | |
| TYPE B | 936 | 800 | WEST | 01 | |
| TYPE B | 695 | 972 | WEST | 01 | |
| TYPE B | 830 | 170 | WEST | 01 | |
| TYPE B | 1000 | 1325 | WEST | 01 | |
| TYPE B | 938 | 775 | WEST | 01 | |
| TYPE B | 898 | 500 | WEST | 01 | |
| TYPE B | 2010 | 1407 | WEST | 01 | |
| TYPE B | 765 | 1276 | WEST | 01 | |
| TYPE B | 608 | 808 | WEST | 01 | |
| TYPE B | 760 | 601 | NORTH | 03 | |
| TYPE C | 76 | 631 | NORTH | 06 | |
| TYPE C | 874 | 746 | NORTH | 01 | |
| TYPE C | 884 | 636 | NORTH | 01 | |
| TYPE C | 891 | 680 | NORTH | 01 | |



SITE KEY PLAN

| SL. NO | DESCRIPTION | PAGE |
|--------|------------------------------|-------|
| 1 | WORK PROGRESS STATUS | 4 |
| 2 | MANPOWER REPORT | 5 |
| 3 | CONCRETE PROCUREMENT | 6 |
| 4 | PROJECT PROGRESS PHOTOGRAPHS | 7-118 |
| 5 | THANK YOU | 119 |

4.0 WORK STATUS REPORT

| Sl.No | Description of works | Total Villas | UNITS | Till Date Completed | % of Complete | Remarks |
|-------|----------------------|--------------|-------|---------------------|---------------|---------|
| 1 | Excavation | 121 | No.s | 105 | 86.78% | |
| 2 | ATT | 121 | No.s | 105 | 86.78% | |
| 3 | Footing PCC | 121 | No.s | 105 | 86.78% | |
| 4 | Footing RCC | 121 | No.s | 102 | 84.30% | |
| 5 | Neck Columns | 121 | No.s | 96 | 79.34% | |
| 6 | Soil Back Filling | 121 | No.s | 85 | 70.25% | |
| 7 | Plinth Beam Filling | 121 | No.s | 75 | 61.98% | |
| 8 | Grade Slab | 121 | No.s | 74 | 61.16% | |
| 9 | G.F Columns | 121 | No.s | 69 | 57.02% | |
| 10 | 1ST Slab | 121 | No.s | 64 | 52.89% | |
| 11 | G.F BRICKWORK | 121 | No.s | 26 | 21.49% | |
| 12 | G.F PLASTERING | 121 | No.s | 3 | 2.48% | |
| 13 | F.F Columns | 121 | No.s | 59 | 48.76% | |
| 14 | 2nd Slab | 121 | No.s | 52 | 42.98% | |
| 15 | S.F Columns | 121 | No.s | 37 | 30.58% | |
| 16 | F.F BRICKWORK | 121 | No.s | 13 | 10.74% | |
| 17 | F.F PLASTERING | 121 | No.s | 4 | 3.31% | |
| 18 | 3rd SLAB | 121 | No.s | 25 | 20.66% | |

LA CITADEL
by

2. MANPOWER REPORT

| S.NO | MANPOWER | 14-10-24 | 15-10-24 | 16-10-24 | 17-10-24 | 18-10-24 | 19-10-24 | 20-10-24 | TOTAL MANPOWER |
|------|------------------------|------------|------------|------------|-----------|------------|------------|------------|-------------------|
| 1 | Masons&Supervisor | 22 | 25 | 20 | 8 | 32 | 45 | 45 | 197 |
| 2 | Carpenters + Helper | 81 | 84 | 95 | 0 | 94 | 95 | 82 | 531 |
| 3 | Barbenders + Helper | 58 | 47 | 48 | 15 | 73 | 92 | 92 | 425 |
| 4 | Unskilled | 79 | 97 | 82 | 27 | 98 | 114 | 112 | 609 |
| 5 | Operators | 10 | 10 | 10 | 10 | 10 | 10 | 10 | 70 |
| 6 | Watertank | 4 | 4 | 4 | 4 | 4 | 4 | 4 | 28 |
| 7 | Electricians | 10 | 10 | 10 | 10 | 10 | 10 | 10 | 70 |
| 8 | Plumbing | 3 | 3 | 3 | 3 | 3 | 5 | 5 | 25 |
| 9 | Tipper drivers&HELPERS | 10 | 10 | 10 | 10 | 10 | 10 | 10 | 70 |
| 10 | Surveyor&Helper | 4 | 4 | 4 | 4 | 4 | 4 | 4 | 28 |
| 12 | granite&Tiles | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| 13 | Texture&Pinters | 8 | 8 | 8 | 0 | 0 | 0 | 0 | 24 |
| | TOTAL | 289 | 302 | 294 | 91 | 338 | 389 | 374 | 2077 |


3. CONCRETE PROCUREMENT



CONCRETE QUANTITY IN SITE

| S.NO | CONCRETE | 14.10.2024 | 15.10.2024 | 16.10.2024 | 17.10.2024 | 18.10.2024 | 19.10.2024 | 20.10.2024 | TOTAL QUANTITY |
|--------------|----------|------------|------------|------------|------------|------------|------------|------------|----------------|
| 1 | P.C.C | 0 | 0 | 7 | 0 | 3 | 6 | 0 | 16 |
| 2 | R.C.C | 24 | 54 | 76 | 0 | 111 | 8 | 38 | 311 |
| TOTAL | | 24 | 54 | 83 | 0 | 114 | 14 | 38 | 327 |

CONCRETE QUANTITY

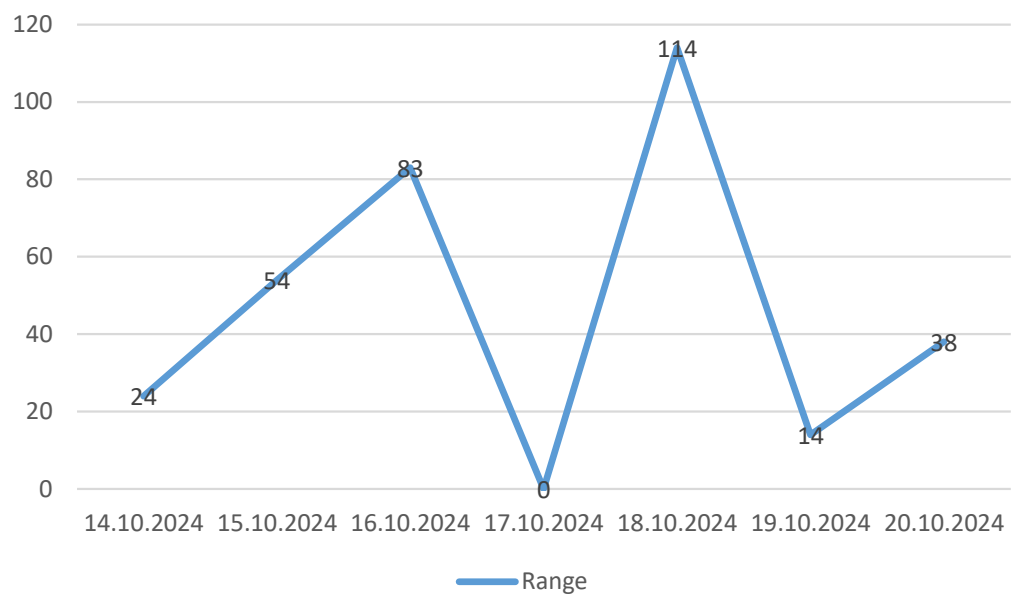

Villa No-5 1st Concrete completed



Villa No-7 3rd Slab Shuttering & F.F Brick Work WIP



Villa No-8 3rd Slab Concrete Completed & G.F Brickwork WIP



Villa No-9 3rd Slab Concrete Completed & G.F WIP



Villa No-11 Footings Concrete Completed



Villa No-12 Soil Backfilling Completed



Villa No-14 Grade Slab WIP



Villa No-15th Grade Slab Concrete Completed



Villa No-18 Grade Slab WIP



Villa No-19 Grade Slab WIP



Villa No-20 F.F Columns Concrete Completed & Brickwork WIP



Villa No-21 2nd Slab Shuttering WIP



Villa No-22 2nd Slab Concrete Completed & G.F WIP



Villa No-23 2nd Slab Concrete & G.F Brickwork Completed



Villa No-24 2nd Slab Concrete Completed & F.F Brickwork WIP



Villa No-25 2nd Slab Concrete Completed & F.F Brickwork WIP



Villa No-26 S.F Columns Concrete Completed & F.F Brickwork WIP



Villa No-27 3rd Slab Shuttering & F.F Brickwork WIP



Villa No-28 Footings PCC Completed



Villa No-29 3rd Slab Concrete Completed



Villa No-30 S.F Columns Concrete & G.F Brickwork Completed



Villa No-31 S.F Columns Completed & G.F Brickwork WIP



Villa No-32 1st Slab Shuttering WIP



Villa No-33 2nd Shuttering WIP



LA CITADEL
by



Villa No-34 Grade Slab Concrete Completed



Villa No-35 Soil Backfilling Completed



Villa No-36 Grade Slab WIP



Villa No-37 External Plastering Completed



Villa No-38 External Plastering Completed



Villa No-39 External Cladding WIP



Villa No-40 External Plastering Completed



Villa No-41 External Plastering WIP



Villa No-42 External Plastering Completed



Villa No-43 S.F Brickwork WIP



Villa No-44 S.F Brickwork WIP



Villa No-45 S.F Brickwork WIP



Villa No-46 S.F Brickwork WIP



Villa No-47 3rd Slab Concrete Completed & G.F Brick Work WIP



Villa No-48 3rd Slab Concrete Completed & G.F Brickwork WIP



Villa No-49 Elevation Slab Concrete Completed & G.F Brickwork WIP



Villa No-50 2nd Slab Shuttering & G.F Brickwork WIP



Villa No-51 Soil Backfilling Completed



Villa No-52 Soil Backfilling Completed



Villa No-53 S.F Columns Concrete Completed & F.F Brickwork WIP



Villa No-54 3rd Slab Concrete Completed & F.F Brick work WIP



Villa No-55 3rd Slab Concrete Completed & F.F Brickwork WIP



Villa No-57 Footing PCC WIP



Villa No-58 Grade Slab Concrete Completed



Villa No-59 F.F Columns Concrete Completed



Villa No: 60 F.F Columns Concrete Completed & G.F Brickwork WIP



Villa No: 61 Soil Backfilling WIP



Villa No: 62 Footings Concrete Completed



Villa No: 63 Footings Concrete Completed



Villa No- 67 Grade Slab WIP



Villa No- 68 2nd Slab Shuttering & G.F WIP



Villa No- 69 2nd Slab Concrete Completed & G.F Brickwork WIP



Villa No-70 3rd Slab Shuttering & F.F Brickwork WIP



Villa No- 71 F.F Brickwork WIP



Villa No- 72 S.F Slab Shuttering & G.F Brickwork WIP



Villa No- 73 Soil Backfilling WIP



Villa No- 74 External Plastering WIP



Villa No- 75 Footings WIP



Villa No- 76 Soil Backfilling WIP



Villa No- 77 Soil Backfilling WIP



Villa No- 79 Soli Backfilling WIP



Villa No- 80 Soil Backfilling WIP



Villa No- 81 Backfilling WIP



Villa No- 82 Soil Backfilling Completed



Villa No- 86 Footing WIP



Villa No- 87 G.F Columns Concrete Completed



Villa No- 88 G.F Columns Concrete Completed



Villa No- 89 1st Slab Concrete Completed



Villa No- 90 2nd Slab Shuttering G.F Brick work WIP



Villa No- 91 1st Slab Concrete Completed



Villa No- 92 2nd Slab Shuttering & G.F Brick WIP



Villa No- 93 2nd Slab Concrete & G.F Brickwork Completed



Villa No-94 3rd Slab Shuttering & F.F Brick Work WIP



Villa No-95 3rd Slab Concrete Completed & F.F Brickwork WIP



Villa No-96 S.F Brick Work WIP



Villa No-97 S.F Brickwork WIP



Villa No-98 External Brickwork Plastering WIP



Villa No-99 S.F Brickwork WIP



Villa No-100 S.F Brickwork WIP



Villa No-101 3rd Slab Shuttering & F.F Brickwork WIP



Villa No-102 Soil Backfilling WIP



Villa No-103 Soil Backfilling WIP



Villa No-104 Plinth Beam Completed



Villa No-105 Grade Slab Concrete Completed



Villa No-106 G.F Columns Shuttering WIP



Villa No-107 1st Slab Shuttering WIP



Villa No-108 F.F Columns Concrete Completed



Villa No-110 S.F Columns Concrete Completed & F.F Brickwork WIP



Villa No-111 S.F Columns Concrete Completed & G.F Brickwork WIP



Villa No-112 2nd Slab Concrete Completed



Villa No-113 S.F Columns & F.F Brickwork WIP



Villa No-114 2nd Slab Concrete Completed & G.F Brickwork WIP



Villa No-115 2nd Slab Concrete Completed & G.F Brickwork WIP



Villa No-117 G.F Columns Concrete Completed



Villa No-122 Soil Backfilling WIP



Villa No-123 Soil Backfilling WIP



Villa No-124 Grade Slab WIP



Villa No- SOUTHWEST NALL SIDE R/W CONCRETE WIP



R/W- SOUTHWEST OFFICE NALL SIDE R/W WIP



Road no-1-7 R/W Raft & Wall WIP



Club House North Retaining Wall WIP



Club House West Retaining Wall WIP



Club House East R/W concrete Casting WIP



Entrance Gate Brickwork Plastering WIP



VILLA- Gate east side R/W WIP





THANK YOU
